Agile Backlog and Sprint Simulation Report

Corporate Mental Wellness and Counseling Platform

Student	SRN	Jira Project	Sprint Window
Debaditya Chakrabarti	PES1UG24CS140	MWP - Mental Wellness Platform	2 Sep 2026 09:00 IST – 8 Sep 2026 18:00 IST

Executive Summary

A dedicated company-managed Scrum project was created in Jira for the Lab 1 scenario, the Corporate Mental Wellness and Counseling Platform. The backlog converts the five functional requirements into three Epics and five User Stories. Each story carries a business priority and a Fibonacci estimate. Sprint 1 was run across the window 2 Sep 2026 09:00 IST to 8 Sep 2026 18:00 IST. Of the 26 planned story points, 13 points are Done, 3 points are In Progress, and 10 points remain To Do at the close of the sprint window.

Jira Workspace Evidence

Project key: MWP. Board: MWP board (Scrum). Sprint: Sprint 1, 2 Sep – 8 Sep 2026. Sprint goal: Deliver the core anonymous counseling booking flow and demonstrate one-week Scrum execution.

Epics

Key	Epic	Purpose
MWP-1	Confidential Identity and Access	Pseudo-ID and privacy-preserving access controls.
MWP-2	Counseling Session Booking	Therapist discovery, confidential booking, and live slot availability.
MWP-3	Wellness and Therapist Schedule Management	Stress assessment, wellness indicators, and therapist appointment management.

Product Backlog and Estimation

Estimates use the Fibonacci scale after a Planning-Poker-style comparison of relative complexity, uncertainty, and implementation effort. High-impact confidentiality and booking capabilities were prioritized first.

Key	User Story	Epic	Priority	Points	Status
MWP-4	Generate anonymous pseudo IDs	MWP-1	High	5	Done
MWP-5	Book a confidential counseling session	MWP-2	High	8	Done
MWP-6	Take a stress assessment and update wellness indicator	MWP-3	Medium	3	In Progress
MWP-7	Refresh unavailable appointment slots	MWP-2	High	5	To Do
MWP-8	Manage therapist appointments	MWP-3	Medium	5	To Do

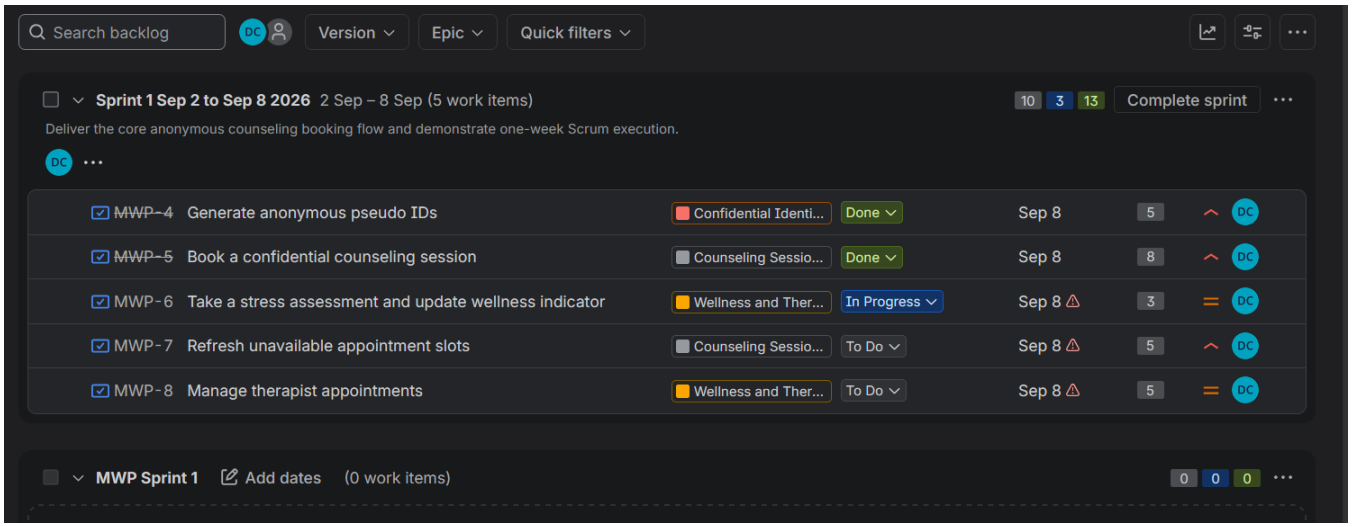


Figure 1. Jira Backlog view — Sprint 1 with Epic links, priority, story points, and status.

User-Story Format

Each backlog item uses the required Agile convention: "As a [role], I want [goal], so that [benefit]." The story descriptions in Jira preserve the employee or therapist viewpoint and link directly to Lab 1 FR-001 through FR-005. The Parent field links every story to its relevant Epic.

Sprint Simulation

The selected stories were placed in Sprint 1. The workflow was simulated in priority order: MWP-4 and MWP-5 moved through In Progress to Done; MWP-6 is In Progress; MWP-7 and MWP-8 remain To Do. This leaves a transparent, reviewable active-board state rather than representing unfinished work as complete.

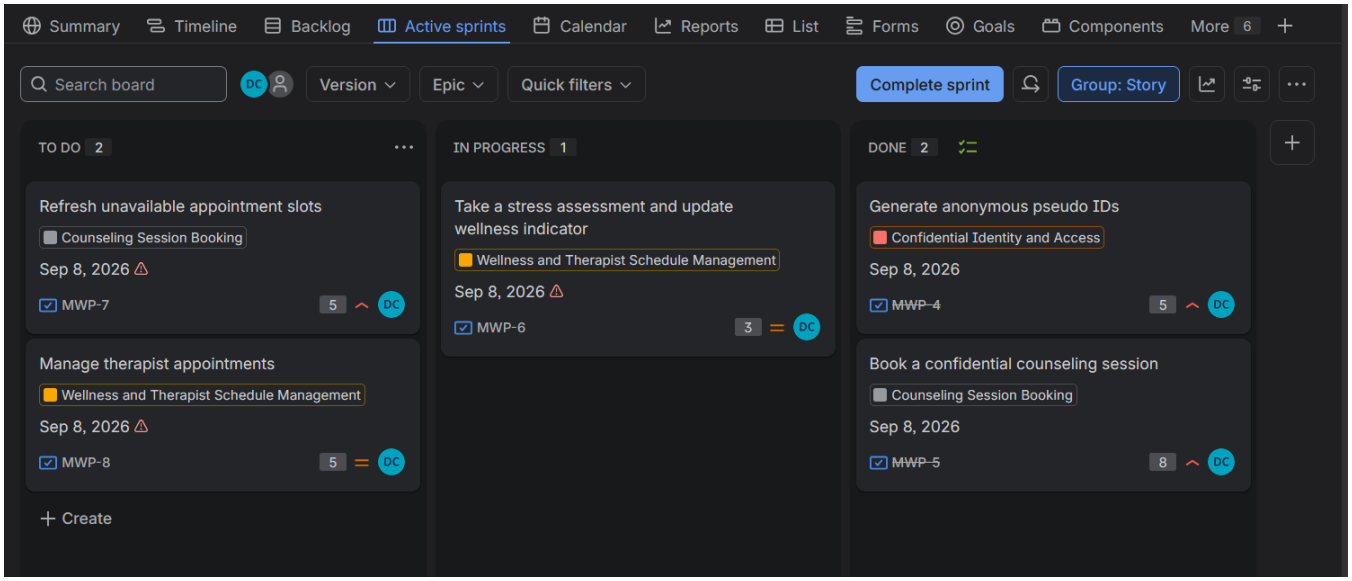


Figure 2. Active Sprint board — To Do / In Progress / Done columns showing the simulated workflow.

Sprint 1 Burndown

The chart below is the live Jira Burndown Chart for Sprint 1 (Reports → Burndown Chart). Because all five stories were added to the sprint scope late in the window and progressed on the same day, the chart shows a flat Remaining Values line

near zero for most of the window, followed by a scope-change jump to 26 points and a sharp drop to 13 points once MWP-4 and MWP-5 were completed.

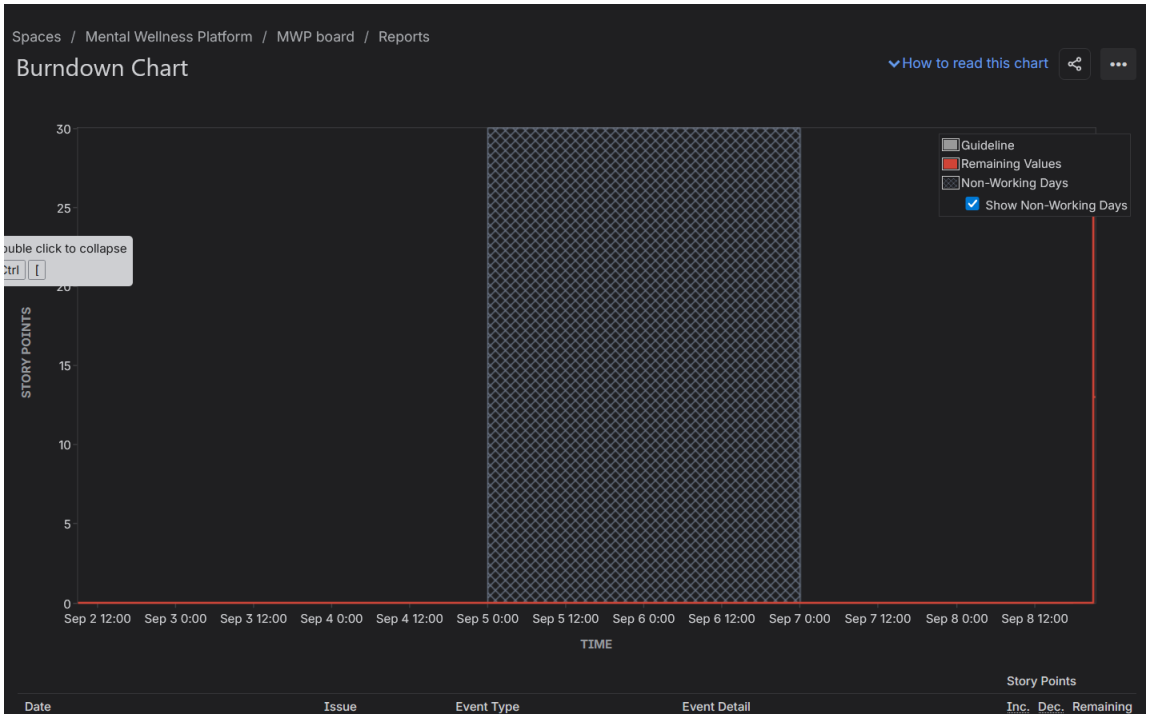


Figure 3. Sprint 1 Burndown Chart (Jira Reports view).

Burndown Interpretation

The actual Remaining Values line stays flat near zero for the bulk of the sprint window because no work was added to the sprint until the final day, then jumps to the full 26-point scope before falling to 13 points once the two highest-priority foundation stories were completed. This differs from a typical steady decline: the pattern reflects a late, single-session scope commitment and simulated completion rather than day-by-day burn-off across the week. The team delivered the two highest-priority foundation stories (13/26 points) but has not met the full sprint forecast; the remaining 13 points (MWP-6, MWP-7, MWP-8) should be carried into the next sprint or re-planned.

Reflection

1. Did the estimations reflect the actual effort?

The 5- and 8-point stories were appropriate relative estimates: pseudo-ID generation was a contained privacy feature, while confidential booking required more workflow integration. The remaining work validates keeping assessment and scheduling management as separate estimates rather than treating the platform as one large item.

2. Was the backlog well prioritized?

Yes. The highest-priority stories protect anonymity and deliver the primary employee outcome: booking a confidential session. The availability-refresh story is also High because it prevents booking conflicts. Assessment and therapist schedule management are Medium because they extend value after the core trust and booking path is available.

3. How did the simulated sprint align with the plan?

The sprint contains the full 26-point forecast. The board shows 13 Done, 3 In Progress, and 10 To Do at the end of the specified window. The planned focus was followed, but the remaining work — and the late scope-addition pattern visible in the burndown — makes the variance visible and supports an evidence-based Sprint 2 plan.

4. What does the burndown say about team capacity?

The team completed 13 points within the simulated window, once work was actually added to the sprint. This is the initial observed velocity for planning the next sprint. A conservative follow-up commitment would be approximately 13 points until more sprint data — ideally planned in from day one of the sprint — confirms whether the late-addition pattern was a reporting artifact of the simulation or a genuine planning constraint.

Instructor Review Checklist

- Project MWP → Backlog: Epic/story links and story-point fields (Figure 1).
- Active sprints: workflow state across To Do / In Progress / Done (Figure 2).
- Reports → Burndown Chart: Sprint 1 burndown (Figures 3).
